Nevada Mercury Air Emissions Control Program

Monday, October 02, 2006
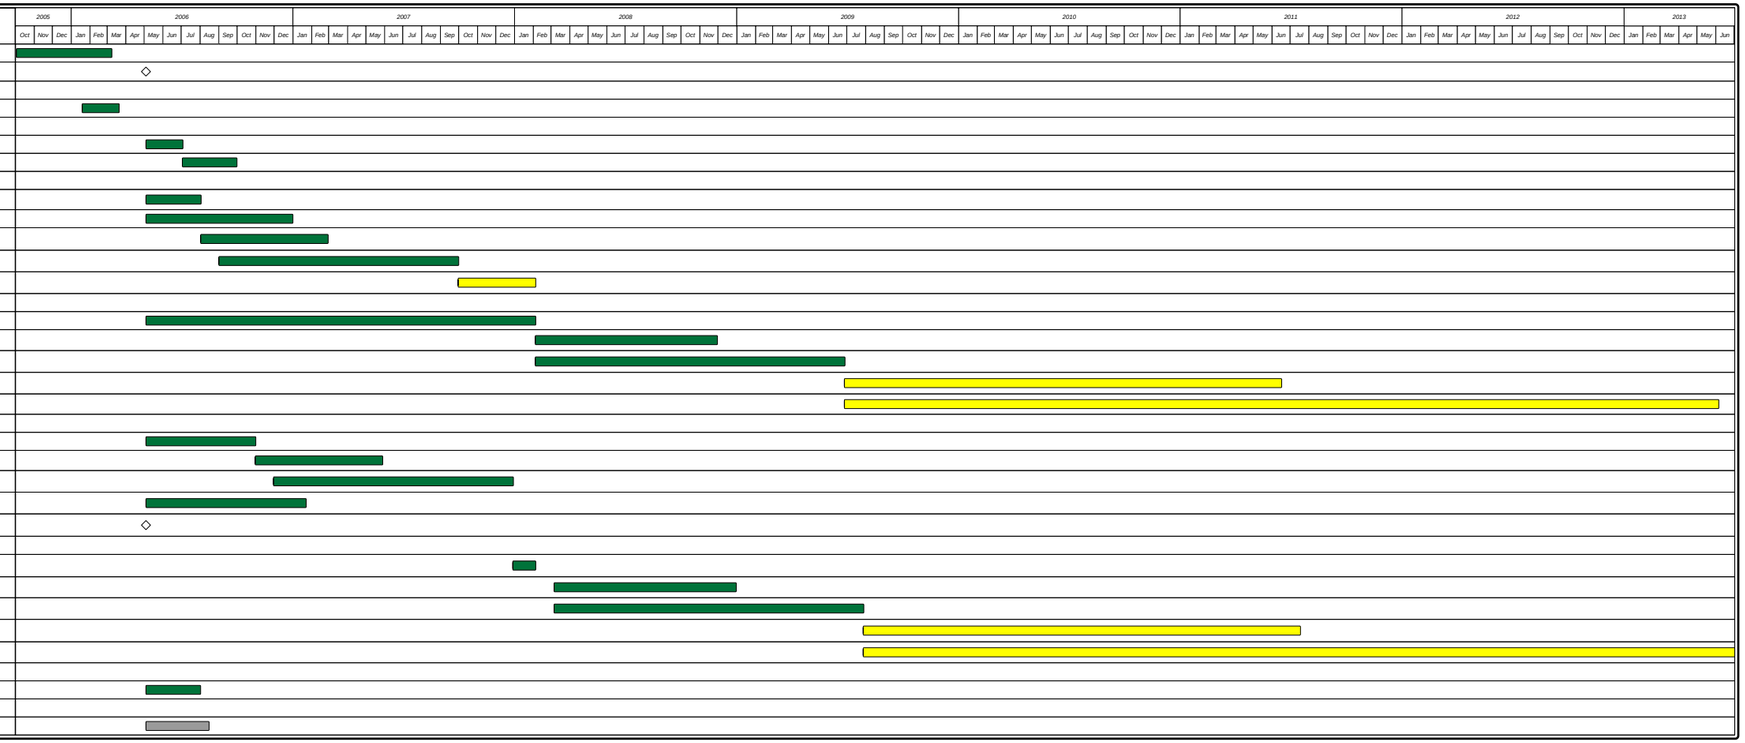
ID	Task Name	Start	Finish	Duration
1	Regulation Development	10/3/2005	3/8/2006	157d
2	Effective Date of Mercury Program (Best Estimate of Date)	5/4/2006	5/4/2006	0d
3				
4	Thermal Mercury Unit Questionaire	1/19/2006	3/20/2006	61d
5				
6	Director's initial determination of De Minimis	5/4/2006	7/3/2006	61d
7	Determination of De Minimis public notice & final action	7/3/2006	9/30/2006	90d
8				
9	Tier-1, Phase-1 Application Filing Period	5/4/2006	8/2/2006	91d
10	Tier -1, Phase-1 Existing Unit Mercury Testing Requirement	5/4/2006	12/31/2006	242d
11	Tier-1, Phase-1 Preliminary Determination of Presumptive NvMACT (30 days for completeness + 180 days process = 210 days)	8/2/2006	2/27/2007	210d
12	Tier-1, Phase-1 Final Action on Application (12 months from DOS [complete date])	9/1/2006	9/30/2007	395d
13	Tier-1, Phase-1 Early Reduction Credit Control Installation Period (Must be installed before Phase-2 app. date of 2/4/2008)	9/30/2007	2/4/2008	128d
14				
15	Tier-1, Phase-2 Application Filing Period	5/4/2006	2/4/2008	642d
16	Tier-1, Phase-2 Preliminary Determination of NvMACT (9 months after DOS [+30 days])	2/4/2008	11/29/2008	300d
17	Tier-1, Phase-2 Final Action on Application (16 months after DOS [+30 days]))	2/4/2008	6/27/2009	510d
18	Tier-1, Phase-2 NvMACT Control Installation Period (Non-ERC) (24 months after permit issuance)	6/27/2009	6/16/2011	720d
19	Tier-1, Phase-2 NvMACT Control Installation Period (With ERC) (48 months after permit issuance)	6/27/2009	6/5/2013	1440d
20				
21	Tier-2, Phase-1 Application Filing Period	5/4/2006	10/31/2006	181d
22	Tier-2, Phase-1 Preliminary Determination of Presumptive NvMACT (30 days for completeness + 180 days to process)	10/31/2006	5/28/2007	210d
23	Tier-2, Phase-1 Final Action on Application (12 months after DOS [|30 days])	11/30/2006	12/29/2007	395d
24	Tier-2, Phase-1 Existing Unit Mercury Testing Requirement ()	5/4/2006	1/22/2007	264d
25	Tier-2, Phase-1 Early Reduction Credit Control Installation Period (Before Phase-2 application date [2/4/2008])	5/4/2006	5/4/2006	0d
26				
27	Tier-2, Phase-2 Application Filing Period (Due before 2/4/2008)	12/29/2007	2/4/2008	38d
28	Tier-2, Phase-2 Preliminary Determination of NvMACT (9 months after DOS [30 days])	3/6/2008	12/30/2008	300d
29	Tier-2, Phase-2 Final Action on Application (16 months after DOS [30 days]))	3/6/2008	7/28/2009	510d
30	Tier-2, Phase-2 NvMACT Control Installation Period (Non-ERC) (24 months after permit issuance)	7/28/2009	7/17/2011	720d
31	Tier-2, Phase-2 NvMACT Control Installation Period (With ERC) (48 months after permit issuance)	7/28/2009	7/6/2013	1440d
32				
33	Tier-3 Application Filing Period	5/4/2006	8/1/2006	90d
34				
35	Fee Determination – Number of Stationary Sources	5/4/2006	8/15/2006	104d
